


LAB 2 — AGILE BACKLOG CREATION & SPRINT SIMULATION IN JIRA

Project Title: Smart Lab Equipment & Slot Reservation Portal

Name: Bestha Venkata Koushik
USN: PES1UG23CS142
Domain: Campus & Academic Operations
Actors: Student, Lab Technician

1.Epics

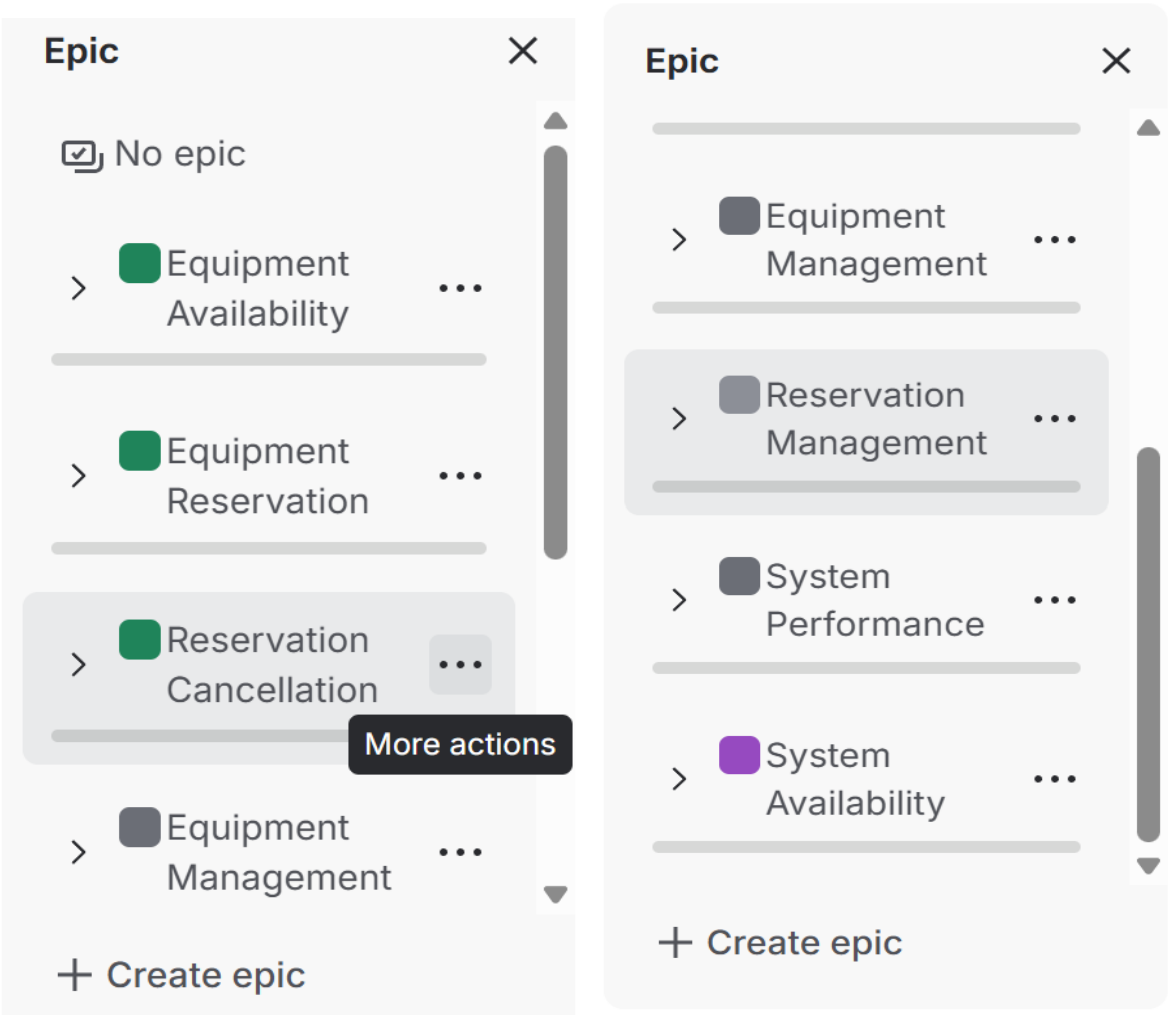


SPRINT 1 — Core Reservation System

Goal: Build the core functionality needed for a student to find equipment and successfully make a reservation.


This screenshot shows a Jira sprint board for 'SLESRP Sprint 1'. The board has a header with a search bar, 'Add dates', '(7 work items)', and a 'Start sprint' button. Below the header, there are 7 work items listed in a table-like format. Each item includes a checkbox, a key (e.g., SLESRP-8), a title, a status (e.g., Equipment Availability), a priority (To Do), and a number (e.g., 3). The items are: SLESRP-8 (1.1: View Equipment Availability), SLESRP-9 (1.2: View Available Reservation ...), SLESRP-10 (2.1: Reserve Equipment and Slot), SLESRP-11 (2.2: Receive Reservation Conf...), SLESRP-14 (4.1: Add and Update Lab Equip...), SLESRP-15 (4.2: Update Equipment Status), and SLESRP-18 (6.1: Fast Availability Information). At the bottom, there is a '+ Create' button and a summary bar showing '7 work items | Estimate: 29'.

Item	Key	Title	Status	Priority	Estimate
✓	SLESRP-8	1.1: View Equipment Availability	Equipment Availability	To Do	3
✓	SLESRP-9	1.2: View Available Reservation ...	Equipment Availability	To Do	3
✓	SLESRP-10	2.1: Reserve Equipment and Slot	Equipment Reserv...	To Do	5
✓	SLESRP-11	2.2: Receive Reservation Conf...	Equipment Reserv...	To Do	3
✓	SLESRP-14	4.1: Add and Update Lab Equip...	Equipment Manag...	To Do	5
✓	SLESRP-15	4.2: Update Equipment Status	Equipment Manag...	To Do	5
✓	SLESRP-18	6.1: Fast Availability Information	System Performan...	To Do	5

This screenshot shows the Jira interface with the 'SLESRP board' selected. The board is in a Kanban view, showing 7 work items in the 'TO DO' column. The items are: 1.1: View Equipment Availability (Equipment Availability, SLESRP-8, 3), 1.2: View Available Reservation Slots (Equipment Availability, SLESRP-9, 3), 2.2: Receive Reservation Confirmation (Equipment Reservation, SLESRP-11, 3), 2.1: Reserve Equipment and Slot (Equipment Reservation, SLESRP-10, 5), 4.2: Update Equipment Status (Equipment Management, SLESRP-15, 5), and 6.1: Fast Availability Information (System Performance, SLESRP-18, 5). The board has a header with a search bar, 'Complete sprint', and 'Group: Story'. The left sidebar shows the Jira navigation menu with options like 'For you', 'Recent', 'Starred', 'Apps', 'Plans', 'Spaces', 'Recent', 'Smart lab Equipment & ...', 'SLESRP board', 'More spaces', 'Recommended', 'Create a roadmap', 'Filters', 'Dashboards', 'Teams', 'Goals', and 'Projects'.

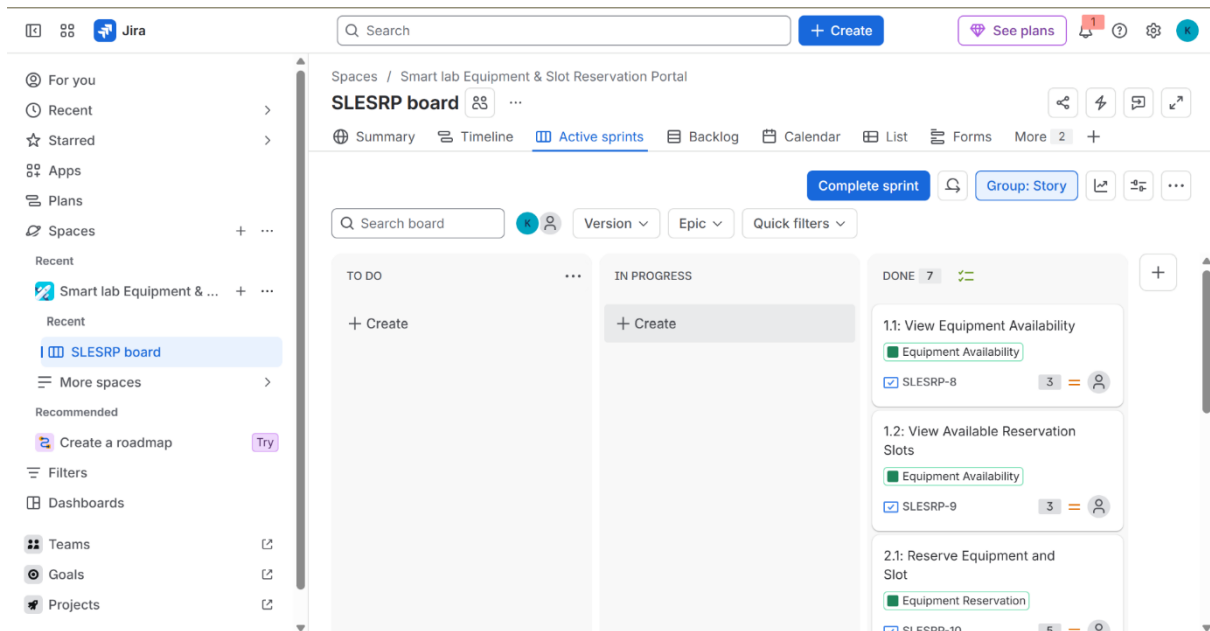

Burndown Chart

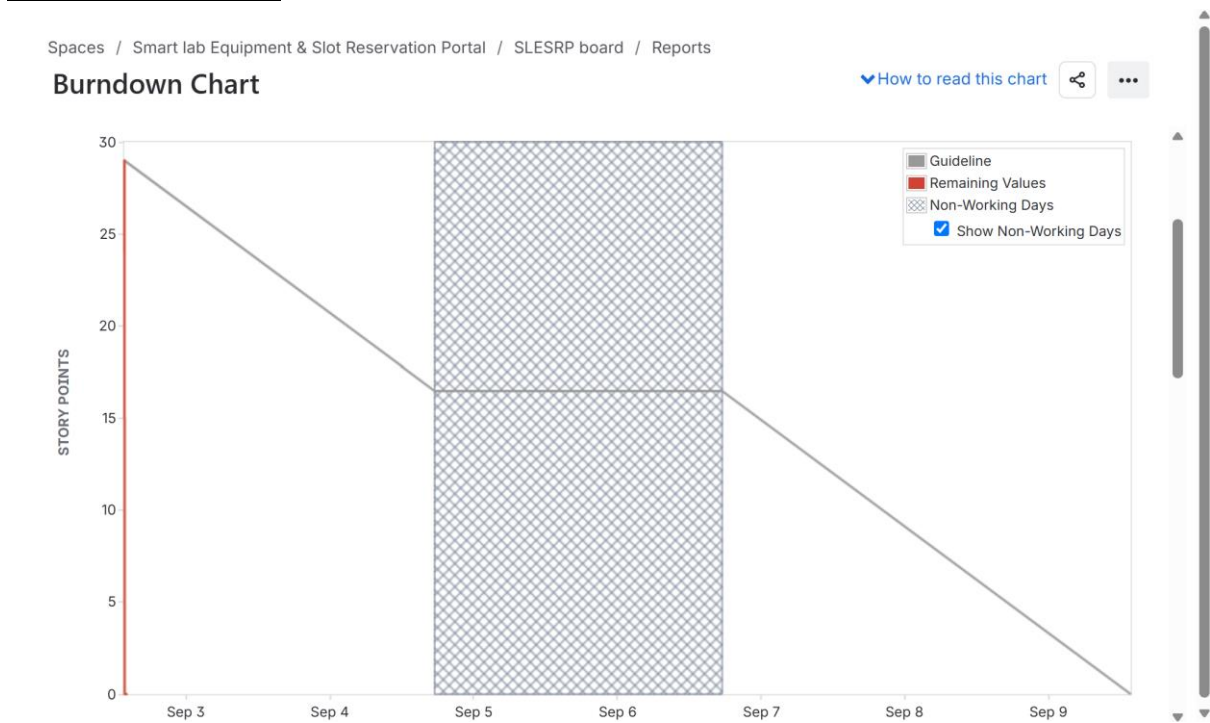

SPRINT 1 — REFLECTION

1. Did your estimations reflect the actual effort?

Answer:

Yes. The Story Point estimates reasonably reflected the actual effort required during Sprint 1. The simpler equipment-availability and reservation tasks were assigned smaller estimates, while more

complex equipment-management work received higher estimates. The Sprint 1 workload was completed successfully, indicating that the estimates were reasonably appropriate.

2. Was your backlog well-prioritized?

Answer:

Yes. The Sprint 1 backlog was prioritized according to user impact and functional importance. Core functions such as viewing equipment availability, viewing reservation slots, reserving equipment, receiving confirmation, and managing equipment were given higher priority because they are essential to the portal's main workflow.

3. How did your simulated sprint align with your plan?

Answer:

Sprint 1 aligned well with the plan. The selected User Stories were placed into the Sprint, and the work was simulated by moving the Stories from **To Do** → **In Progress** → **Done**. The planned core reservation functionality was completed within the Sprint.

4. What insights did the Burndown Chart give about your team's capacity?

Answer:

The Burndown Chart showed how the remaining Story Points decreased as Sprint 1 work was completed. It indicated that the team was able to complete the planned workload and provided an indication of the team's capacity for handling similar work in future Sprints.

SPRINT 2 — Management, Cancellation & Reliability

Goal: Complete the remaining reservation lifecycle, technician management functions, and system reliability requirements.

☐	SLESRP Sprint 2	9 Sep – 16 Sep (7 work items)		31	0	0	Start sprint	...
☒	SLESRP-12	3.1: Cancel Existing Reservation	Reservati...	To Do	3	=		
☒	SLESRP-13	3.2: Release Cancelled Slot	Reservati...	To Do	3	=		
☒	SLESRP-16	5.1: View Student Reservations	Reservati...	To Do	5	=		
☒	SLESRP-17	5.2: Manage Student Reservations	Reservati...	To Do	5	=		
☒	SLESRP-19	6.2: Fast Reservation Information	System P...	To Do	5	=		
☒	SLESRP-20	7.1: Reliable Student Access	System A...	To Do	5	=		
☒	SLESRP-21	7.2: Reliable Technician Access	System A...	To Do	5	=		
+ Create								

For you

Recent

Starred

Apps

Plans

Spaces

Recent

Smart lab Equipment & ...

Recent

SLESRP board

More spaces

Recommended

Create a roadmap

Filters

Dashboards

Teams

Goals

Projects

Search

Create

See plans

Spaces / Smart lab Equipment & Slot Reservation Portal

SLESRP board

Summary Timeline Active sprints Backlog Calendar List Forms More

Complete sprint

Group: Story

Search board

Version

Epic

Quick filters

TO DO 2

3.1: Cancel Existing Reservation

Reservation Cancellation

SLESRP-12

3.2: Release Cancelled Slot

Reservation Cancellation

SLESRP-13

IN PROGRESS 5

5.1: View Student Reservations

Reservation Management

SLESRP-16

5.2: Manage Student Reservations

Reservation Management


SLESRP-17

6.2: Fast Reservation Information


System Performance

SLESRP-19

DONE

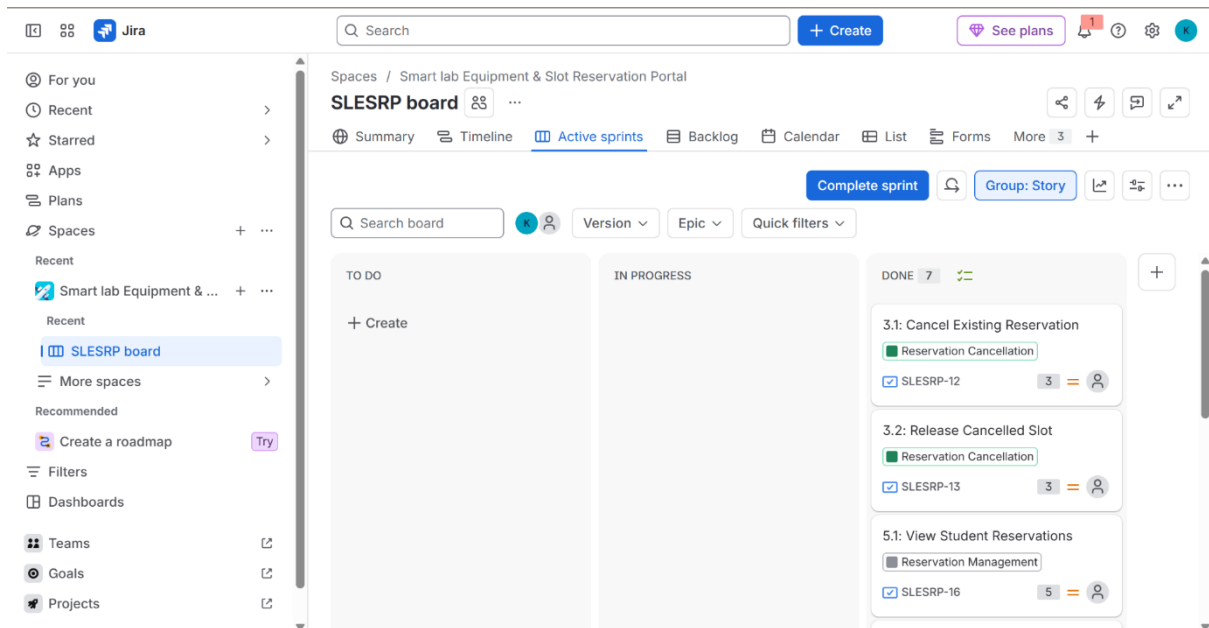

Burndown Chart

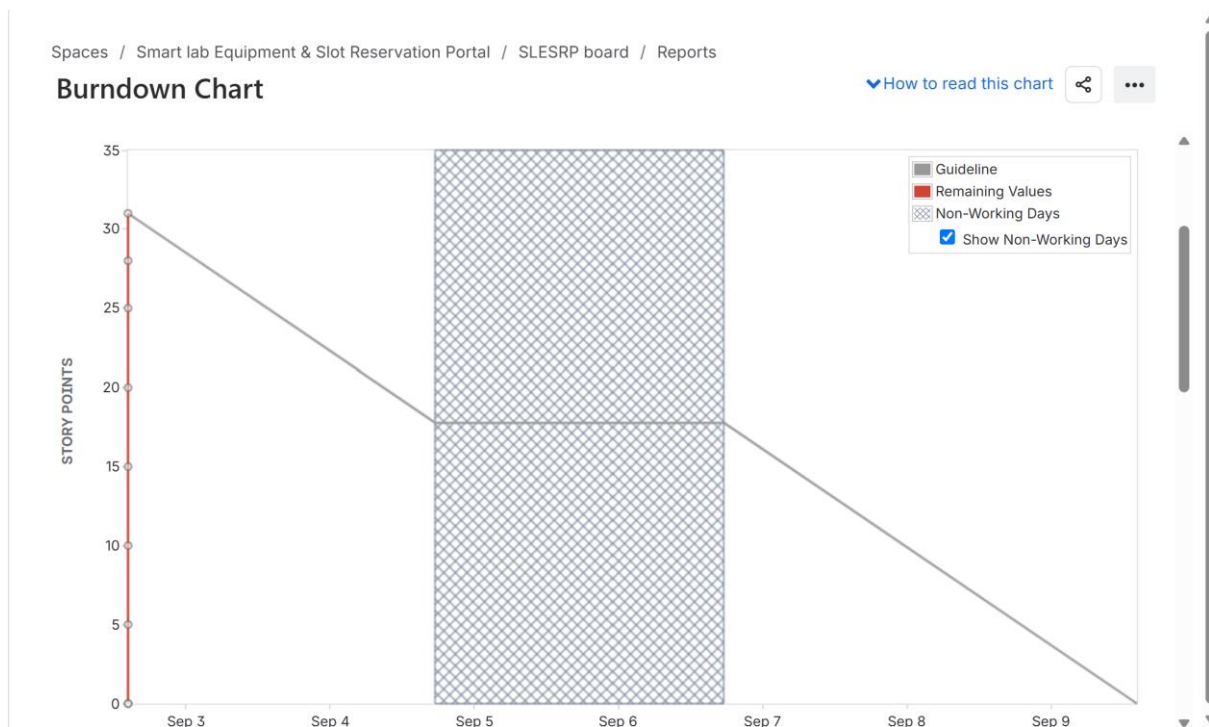

SPRINT 2 — REFLECTION

1. Did your estimations reflect the actual effort?

Answer:

Yes. The Sprint 2 estimates were reasonably consistent with the actual effort. The cancellation and reservation-management stories were given moderate estimates, while the system performance and

availability stories required higher estimates because they involved additional complexity and reliability requirements. The Sprint was successfully completed.

2. Was your backlog well-prioritized?

Answer:

Yes. Sprint 2 focused on the remaining reservation lifecycle, technician management, system performance, and system availability requirements. The higher-priority technician and reliability functions were included along with the medium-priority reservation-cancellation functions, giving the Sprint a balanced set of important tasks.

3. How did your simulated sprint align with your plan?

Answer:

Sprint 2 followed the planned Agile workflow. The selected User Stories were added to Sprint 2, started as planned, and progressed through **To Do → In Progress → Done** before the Sprint was completed. The Sprint therefore aligned well with the planned objectives.

4. What insights did the Burndown Chart give about your team's capacity?

Answer:

The Sprint 2 Burndown Chart showed the remaining Story Points against the ideal guideline. The chart indicated that the team was able to complete the planned Sprint work. It also showed that work was completed relatively quickly, which suggests that the team had sufficient capacity for the amount of work committed to the Sprint. The lab notes that early completion can indicate that a team may not be committing to enough work during Sprint planning.
